21	Providing and laying/fixing cement base, precast, pre polished cement concrete, designer tiles 25mm thick	Sqm	100.00	8/May/17	23/May/17	15
22	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114	No.	89.00	8/May/17	28/May/17	20
23	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete	Sqm	14.00	9/May/17	30/May/17	21
24	SUPPLYING AND FIXING OF LEG PRESS DOUBLE OF SAFE AREA : 2.8MTR X 1.5 MTR, CENTRE PIPE :	No.	1.00	30/May/17	4/Jun/17	5
25	SUPPLYING AND FIXING OF FUN WALKER DOUBLE OF SAFE AEA : 3 MTR X 2 MTR, MAIN	No.	1.00	30/May/17	4/Jun/17	5
26	SUPPLYING AND FIXING OF PENDULUM DOUBLE OF SAFE AREA : 2.5 MTR X 1 MTR, MAIN FRAME : 100	No.	1.00	30/May/17	4/Jun/17	5
27	SUPPLYING AND FIXING OF CYCLE TWO WAY OF SAFE AREA : 2.5 MTR X 1 MTR, MAIN FRAME : 100	No.	1.00	30/May/17	4/Jun/17	5
28	SUPPLYING AND FIXING OF TAI CHI SPINEER DOUBLE OF SAFE AREA : 2 MTR. DIA, MAIN FRAME	No.	1.00	30/May/17	4/Jun/17	5
29	SUPPLYING AND FIXING OF TWISTER THREE WAY OF SAFE AREA : 2.5 MTR. DIA, MAIN FRAME : 100 NB	No.	1.00	30/May/17	4/Jun/17	5
30	SUPPLYING AND FIXING OF CHEST PRESS DOUBLE – OF SAFE AREA : 4 MTR X 2.5 MTR, OF	No.	1.00	30/May/17	4/Jun/17	5
31	SUPPLYING AND FIXING OF FUN ROVER, SAFE AREA : 2.5 MTR X 1.5 MTR., MAIN FRAME : 80 NB GI	No.	1.00	30/May/17	4/Jun/17	5
32	SUPPLYING AND FIXING OF FUN RIDER, SAFE AREA: 2.5 MTR X 1.5 MTR., MAIN FRAME: 80 NB GI B-	No.	1.00	30/May/17	4/Jun/17	5
33	Removing BS Slab of drain and Stacking	Sqm	170.10	31-Jan-17	10/Mar/17	38
34	Refixing Stone Slabs of drains and Pointing in C.M(1:3)	Sqm	170.10	2/Feb/17	25/Mar/17	51
35	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an	Cum.	1106.19	7/Feb/17	3/Apr/17	55
36	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry,	Cum.	1454.47	2/Feb/17	12/Feb/17	10
37	Providing and laying in position plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with 20mm and down	Cum.	112.25	9/Feb/17	5/Apr/17	55
38	Providing and laying cement concrete using 20mm and down size granite coarse aggregates and fine aggregates of ready	Cum.	258.77	11/Feb/17	12/Apr/17	60
39	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface	Sqm	2546.50	16/Feb/17	12/Apr/17	55
40	Providing T .M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in	Tonne	17.15	21/Feb/17	17/Apr/17	55
41	Providing granite slabs of selected quality roughly dressed and fixed in cement mortar (1:6) including fixing curing etc.,	Sqm	633.60	23/Feb/17	25/Mar/17	30
42	Providing Machine cutting for BS slab including all lead and lift as per direction of Engginner-in charge of work -Data Rate	Sqm	3906.00	24/Feb/17	26/Mar/17	30
43	Providing precast slab of 250mm thick including cost of all materials, labour, curing, transportation, loading ,unloading,	Sqm	37.80	1/Mar/17	16/Mar/17	15
44	Excavation for roadwork in all type of soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and	Cum.	727.24	11/Mar/17	15/Apr/17	35
45	Providing and laying in position plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with 40mm and down	Cum.	727.24	13/Mar/17	12/Apr/17	30

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯಶವಂತಪುರ ಉಪ ವಿಭಾಗ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by CamScanner

23	enamel paint in approved shades on new plastered concrete	Sqm				
24	SUPPLYING AND FIXING OF LEG PRESS DOUBLE OF SAFE AREA : 2.8MTR X 1.5 MTR, CENTRE PIPE :	No.	1.00	30/May/17	4/Jun/17	5
25	SUPPLYING AND FIXING OF FUN WALKER DOUBLE OF SAFE AEA : 3 MTR X 2 MTR, MAIN	No.	1.00	30/May/17	4/Jun/17	5
26	SUPPLYING AND FIXING OF PENDULUM DOUBLE OF SAFE AREA : 2.5 MTR X 1 MTR, MAIN FRAME : 100	No.	1.00	30/May/17	4/Jun/17	5
27	SUPPLYING AND FIXING OF CYCLE TWO WAY OF SAFE AREA : 2.5 MTR X 1 MTR, MAIN FRAME : 100	No.	1.00	30/May/17	4/Jun/17	5
28	SUPPLYING AND FIXING OF TAI CHI SPINEER DOUBLE OF SAFE AREA : 2 MTR DIA, MAIN FRAME	No.	1.00	30/May/17	4/Jun/17	5
29	SUPPLYING AND FIXING OF TWISTER THREE WAY OF SAFE AREA : 2.5 MTR. DIA, MAIN FRAME : 100 NB	No.	1.00	30/May/17	4/Jun/17	5
30	SUPPLYING AND FIXING OF CHEST PRESS DOUBLE – OF SAFE AREA : 4 MTR X 2.5 MTR, OF	No.	1.00	30/May/17	4/Jun/17	5
31	SUPPLYING AND FIXING OF FUN ROVER, SAFE AREA : 2.5 MTR X 1.5 MTR., MAIN FRAME : 80 NB GI	No.	1.00	30/May/17	4/Jun/17	5
32	SUPPLYING AND FIXING OF FUN RIDER, SAFE AREA: 2.5 MTR X 1.5 MTR., MAIN FRAME: 80 NB GI B-	No.	1.00	30/May/17	4/Jun/17	5
33	Removing BS Slab of drain and Stacking	Sqm	170.10	31-Jan-17	10/Mar/17	38
34	Refixing Stone Slabs of drains and Pointing in C.M(1:3)	Sqm	170.10	2/Feb/17	25/Mar/17	51
35	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an	Cum.	1106.19	7/Feb/17	3/Apr/17	55
36	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry,	Cum.	1454.47	2/Feb/17	12/Feb/17	10
37	Providing and laying in position plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with 20mm and down	Cum.	112.25	9/Feb/17	5/Apr/17	55
38	Providing and laying cement concrete using 20mm and down size granite coarse aggregates and fine aggregates of ready	Cum.	258.77	11/Feb/17	12/Apr/17	60
39	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface	Sqm	2546.50	16/Feb/17	12/Apr/17	55
40	Providing T .M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in	Tonne	17.15	21/Feb/17	17/Apr/17	55
41	Providing granite slabs of selected quality roughly dressed and fixed in cement mortar (1:6) including fixing curing etc.,	Sqm	633.60	23/Feb/17	25/Mar/17	30
42	Providing Machine cutting for BS slab including all lead and lift as per direction of Engineer-in charge of work -Data Rate	Sqm	3906.00	24/Feb/17	26/Mar/17	30
43	Providing precast slab of 250mm thick including cost of all materials, labour, curing, transportation, loading ,unloading,	Sqm	37.80	1/Mar/17	16/Mar/17	15
44	Excavation for roadwork in all type of soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and	Cum.	727.24	11/Mar/17	15/Apr/17	35
45	Providing and laying in position plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with 40mm and down	Cum.	727.24	13/Mar/17	12/Apr/17	30
46	Construction of reinforced, dowel jointed, plain cement concrete pavement over a prepared sub base with OPC	Cum.	1090.85	15/Mar/17	9/Apr/17	25
47	providing vaccum dewatering concrete as per direction of engineer in charge of thework	Sqm	7272.35	16/Mar/17	10/Apr/17	25
48	Providing groove cutting for width of 5mm to 10mm and depth 80mm- 100mm including cost of cutting machine,	rmt	3264.30	17/Mar/17	20/Apr/17	34
49	Providing and erecting direction and place identification retro-reflectorised sign as per IRC :67-2012 made of high intensity	Sqm	2.00	17/Mar/17	19/Mar/17	2

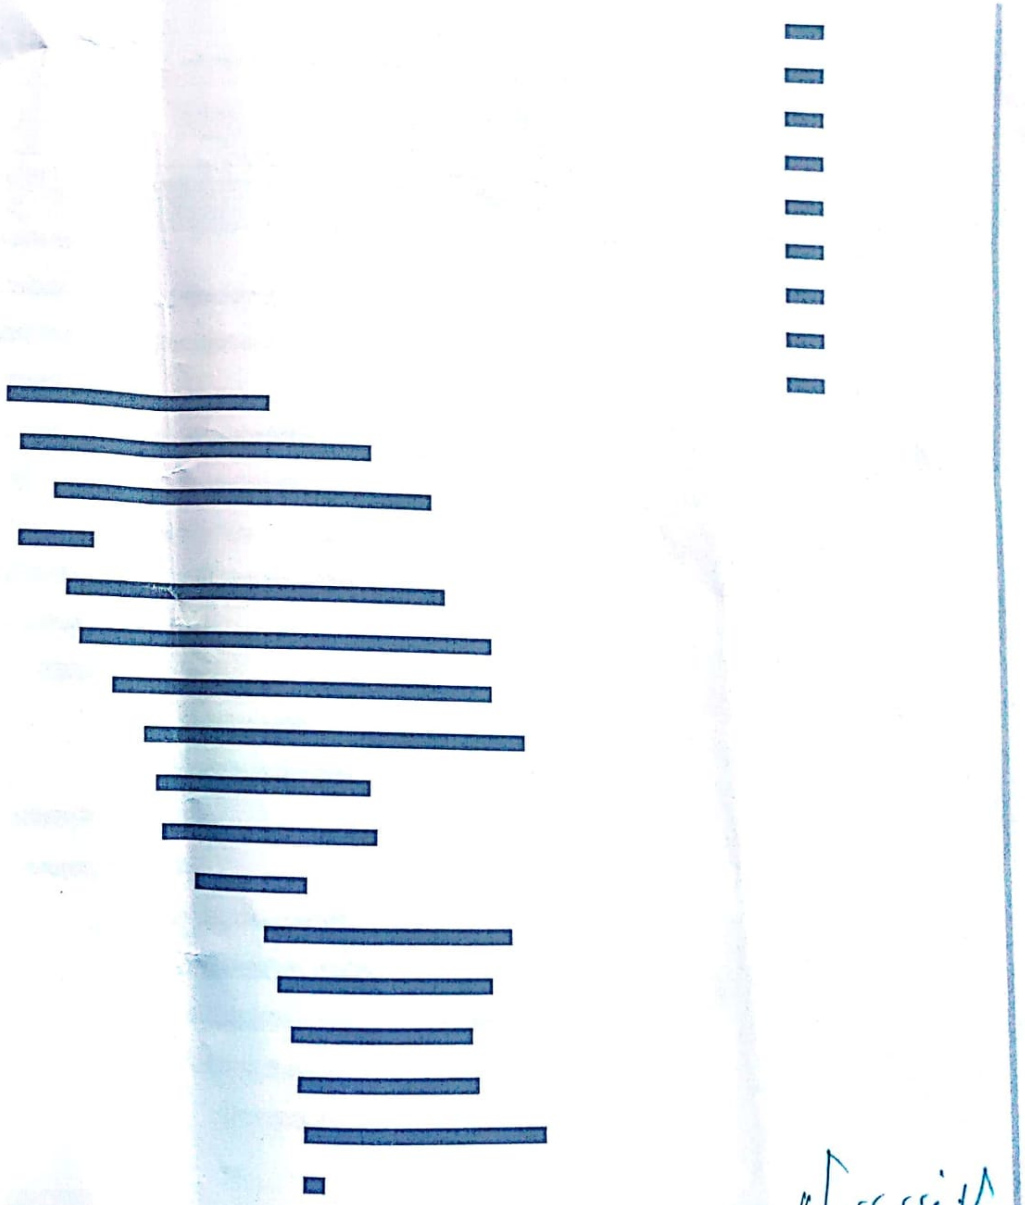

Time Table For Work Complete

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯಶವಂತಪುರ ಉಪ ವಿಭಾಗ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by CamScanner

CIVIL QUALITY CONSULTANTS AND ENGINEERS
PROJECT PLANNING/SCHEDULE

Client Name : Sri.N.M Krishna Murthy

Project Name : Improvements to road, drain and other works in Khatha Nagar in Ward no 16 and Improvements to Road drain and other works in Siddharta Nagar, Peenya Plantation in Ward no 16.

Project Manager /Team Leader : Hemanth

Project Start Date : 11-Jan-17

Project End Date : 10-Jun-17

Project Length in Days : 150 Include Monsoon

Sl. No	Assignment	Unit	Boq Qnty	Start Date	End Date	No. of Working Days
1	Removing BS Slab of drain and Stacking	Sqm	105.30	13-Jan-17	20/Feb/17	38
2	Refixing Stone Slabs of drains and Pointing in C.M(1:3)	Sqm	105.30	20/Jan/17	12/Mar/17	51
3	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an	Cum.	263.17	15/Jan/17	11/Mar/17	55
4	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry,	Cum.	809.59	23/Jan/17	17/Feb/17	25
5	Providing and laying in position plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with 20mm and down	Cum.	37.95	20/Jan/17	16/Mar/17	55
6	Providing and laying cement concrete using 20mm and down size granite coarse aggregates and fine aggregates of ready	Cum	41.77	16/Jan/17	17/Mar/17	60
7	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface	Sqm	273.00	25/Jan/17	21/Mar/17	55
8	Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in	Tonne	2.53	26/Jan/17	22/Mar/17	55
9	Providing and constructing precast concrete solid blocks with compressive strength not less than 35 Kg/sqm with cement	Sqm	144.00	30/Jan/17	1/Mar/17	30
10	Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size	Cum.	3.60	4/Feb/17	4/Mar/17	28
11	Providing precast slab of 100 mm thick including cost of all materials, labour, curing, transportation, loading , unloading,	Sqm	304.30	15/Feb/17	20/Mar/17	33
12	Providing precast slab of 250mm thick including cost of all materials, labour, curing, transportation, loading , unloading,	Sqm	23.40	25/Feb/17	22/Mar/17	25
13	Providing 15mm thick cement plaster in single coat with cement mortar 1:3 , to brick masonry including rounding off	Sqm	67.20	1/Feb/17	3/Mar/17	30
14	Providing and fixing 20mm thick and maximum width of 1200mm gang saw water cut sadarhalli grey granite in CM 1:4	Sqm	175.20	3/Feb/17	28/Feb/17	25
15	Excavation for roadwork in all type of soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and	Cum.	404.79	25/Feb/17	1/Apr/17	35
16	Providing and laying in position plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with 40mm and down	Cum.	404.79	26/Feb/17	1/Apr/17	34
17	Cement concrete pavement. Construction of un-reinforced plain cement concrete pavement,thickness as per design, over	Cum.	607.19	27/Feb/17	23/Apr/17	55
18	providing vaccum dewatering concrete as per direction of engineer in charge of thework	Sqm	4047.93	28/Feb/17	4/May/17	65
19	Providing groove cutting for width of 5mm to 10mm and depth 80mm- 100mm including cost of cutting machine,	rmt	1757.02	5/Mar/17	8/May/17	64
20	Providing and erecting direction and place identification retro reflectorised sign as per IRC :67-2012 made of high intensity	Sqm	2.00	6/May/17	16/May/17	10
21	Providing and laying/fixing cement base, precast, pre polished cement concrete, designer tiles 25mm thick	Sqm	100.00	8/May/17	23/May/17	15
22	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114	No.	89.00	8/May/17	28/May/17	20
	Painting two coats after filling the surface with synthetic	Sqm	14.00	9/May/17	30/May/17	21

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯಶವಂತಪುರ ಉಪ ವಿಭಾಗ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by CamScanner

Clients Name

Project Name : Sri.N.M Krishna Murthy

Project Manager /Team Leader : Improvements to road, drain and other works in Khatha Nagar in Ward no 16 and Improvements to Road drain and other works in Siddharta Nagar, Pennya Plantation in Ward no 16.

Project Start Date : Hemanth

Project End Date : 11-Jan-17

Project Length in Days : 10-Jun-17

: 150

Include Alonsoon

CIVIL QUALITY CONSULTANTS AND ENGINEERS

PROJECT PLANNING/SCHEDULE

Sl. No	Assignment	Unit	Qnty	Start Date	End Date	No. of Working Days
1	Removing 85 Slab of drain and Sucking	Sqm	105.30	13-Jan-17	20/Feb/17	38
2	Kicking Stone Slabs of drains and Pointing in CM(1:3)	Sqm	105.30	20/Jan/17	12/Mar/17	51
3	Earthwork excavation by manual means in ordinary soil investing an average horizontal throw upto 2 meters and an	Cum.	263.17	15/Jan/17	11/Mar/17	55
4	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry.	Cum	809.59	23/Jan/17	17/Feb/17	25
5	Providing and laying m position plain cement concrete of mix1:3.6 with OPC cement @ 220kgs. with 20mm and down	Cum.	37.95	20/Jan/17	16/Mar/17	55
6	Providing and laying cement concrete using 20mm and down size granite coarse aggregates and fine aggregates of ready	Cum	41.77	16/Jan/17	17/Mar/17	60
7	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface	Sqm	2730.00	25/Jan/17	21/Mar/17	55
8	Providing ? .M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in	Tonne	2.53	26/Jan/17	22/Mar/17	55
9	Providing and consructing precast concrete solid blocks with compressive strength not kse than 35 Kg/sqm with cement	Sqm	1440.00	30/Jan/17	1/Mar/17	30
10	Providing and laying m position plain cement concrete of mix 1:2:4 with cement @ 240kgs. with 20mm and down size	Cum	3.60	4/Feb/17	4/Mar/17	28
11	Providing precast slab of 100 mm thick including cost of all materials, labour, curing, transportation, loading, unloading,	Sqm	3043.0	15/Feb/17	20/Mar/17	33
12	Providing precast slab of 25mm thick including cost of all materials, labour, curing, transportation, loading, unloading,	Sqm	23.40	25/Feb/17	22/Mar/17	25
13	Providing 15mm thick cement plaster m angle coat with cement mortar 1:3, to brick masonry including roundinf off	Sqm	67.20	1/Feb/17	3/Mar/17	30
14	Providing and fixing 20mm thick and minimum width of 120mm gang saw water cut sadarhalli grey granite in CM 1:4	Sqm	1752.0	3/Feb/17	28/Feb/17	25
15	Excavation for roadwork in all type of soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and	Cum	404.79	25/Feb/17	1/Apr/17	35
16	Providing and laying m position plain cement concrete of mix1:3.6 with OPC cement @ 220kgs, with 40mm and down	Cum	404.79	26/Feb/17	1/Apr/17	34
17	Cement concrete pavement. Construction of un-reinforced plain cement concrete pavement,thickness as per design, over	Cum	607.19	27/Feb/17	23/Apr/17	55
18	Providing vacuum dewatering concrete as per direction of engineer in charge of thework	Sqm	4047.93	28/Feb/17	4/May/17	65
19	Providing groove cutting for width of 5mm to 10mm and depth 80mm- 100mm including cost of cutting machine,	mm	1757.02	5/Mar/17	8/May/17	64

Scanned by CamScanner

47	providing vaccum dewatering concrete as per direction of engineer in charge of thework	Sqm	7272.35	16/Mar/17	10/Apr/17	25
48	Providing groove cutting for width of 5mm to 10mm and depth 80mm- 100mm including cost of cutting machine,	rmt	3264.30	17/Mar/17	20/Apr/17	34
49	Providing and erecting direction and place identification retro-reflectorised sign as per IRC :67-2012 made of high intensity	Sqm	2.00	17/Mar/17	19/Mar/17	2

[redacted]

[redacted]

[redacted]

[redacted]

[redacted] Time Table For Work Complete

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಧಿಕಾರಿಗಳು
ಯಶವಂತಪುರ ಉಪ ವಿಭಾಗ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by CamScanner
